


FedAuth-2004-06-15

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	er					September			J	
							11/9	January	May	8/29	10/17	12/5	12/28	2/15	4/4	5/23
1	Project Start	0 days	Mon 2/2/04	Mon 2/2/04												
2	Identify group members	7 days	Mon 2/2/04	Tue 2/10/04	1	Walker,Harel										
3	First group meeting	1 day	Mon 3/8/04	Mon 3/8/04	2	All										
4	Distribute meeting notes	7 days	Tue 3/9/04	Wed 3/17/04	3	Walker										
5	Schedule conference call	7 days	Thu 3/18/04	Fri 3/26/04	4	Walker										
6	Conference call #1	0 days	Thu 4/8/04	Thu 4/8/04	5	All										
7	Distribute plan to ITLC	5 days	Thu 4/8/04	Wed 4/14/04	6	Walker,Harel										
8	Sub-project plans to DW	4 days	Thu 4/8/04	Tue 4/13/04	6	All										
9	Draft project schedule	5 days	Thu 4/8/04	Wed 4/14/04	6	Walker,Harel										
10	Conference call - review schedule	0 days	Wed 4/21/04	Wed 4/21/04	9,8	All										
11	Distribute schedule to ITLC	2 days	Thu 4/22/04	Fri 4/23/04	10	Walker,Harel										
12	ITLC approval to proceed	1 day	Mon 4/26/04	Mon 4/26/04	11	ITLC										
13	UCFY / YBO	75 days	Tue 4/27/04	Mon 8/9/04	12											
14	Configure Shibboleth Apache module	2 wks	Tue 4/27/04	Mon 5/10/04		Kini										
15	Implement Shib/Apache instance of JAAS	7 wks	Tue 5/11/04	Mon 6/28/04	14	Kini										
16	Integrate JAAS into UCFY	9 wks	Tue 4/27/04	Mon 6/28/04		Barman										
17	Initial integration testing	1 wk	Tue 6/29/04	Mon 7/5/04	15,16	Kini,Barman										
18	Integration testing w/ campuses	5 wks	Tue 7/6/04	Mon 8/9/04	17	Kini,Barman										
19	Develop user documentation	3 wks	Tue 7/6/04	Mon 7/26/04	17	Barman										
20	Train support personnel	1 wk	Tue 7/27/04	Mon 8/2/04	19	Barman										
21	Move to production environment	1 wk	Tue 8/3/04	Mon 8/9/04	38,51	Barman										
22	CDL-licensed resources	1 day	Tue 4/27/04	Tue 4/27/04	12											
23	TBD	1 day	Tue 4/27/04	Tue 4/27/04												
24	Policy	25 days	Mon 4/26/04	Mon 5/31/04	12											
25	Decision to reverify ID in UCFY (pilot)	0 days	Mon 4/26/04	Mon 4/26/04		Baptista,James,W										
26	Develop campus policy questionnaire	0 days	Mon 4/26/04	Mon 4/26/04		Craig,Wasley										
27	Campuses respond to questionnaire	25 days	Tue 4/27/04	Mon 5/31/04												
28	UCI	5 wks	Tue 4/27/04	Mon 5/31/04		Roode,Arseniev										
29	UCLA	5 wks	Tue 4/27/04	Mon 5/31/04		Wu										
30	UCSD	5 wks	Tue 4/27/04	Mon 5/31/04		Lawrence										

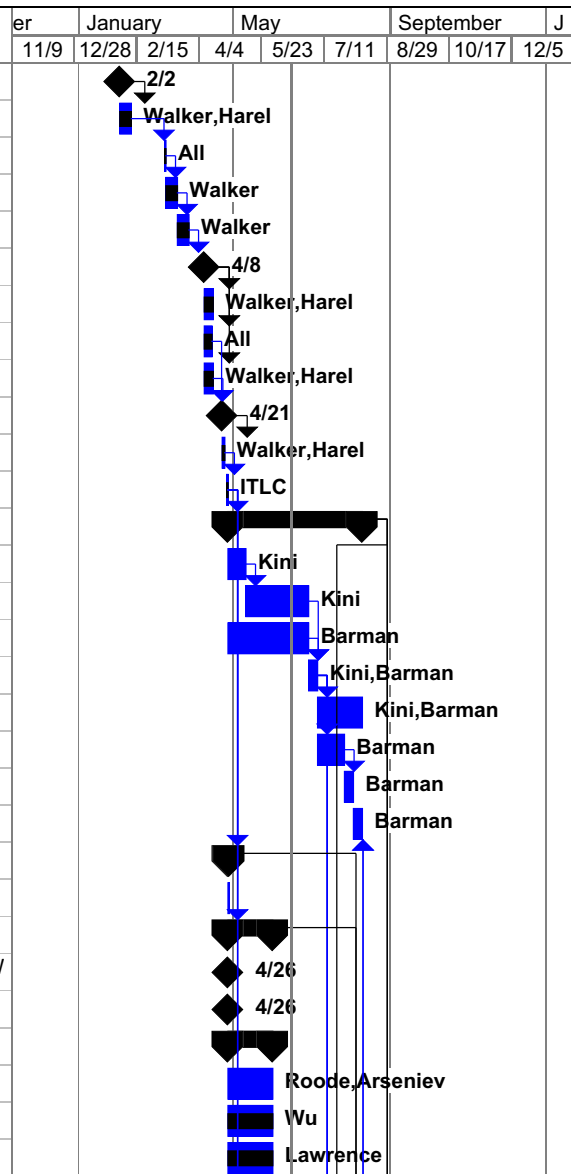

Project: UC Federated Authentication Date: Tue 6/15/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

FedAuth-2004-06-15

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	er			January			May			September			J	
							11/9	12/28	2/15	4/4	5/23	7/11	8/29	10/17	12/5					
31	✓ Presentation to COVCA	0 days	Thu 5/27/04	Thu 5/27/04																
32	UCSD	80 days	Tue 4/27/04	Mon 8/16/04	12															
33	✓ Install core Shibboleth Origin	1 day	Tue 4/27/04	Tue 4/27/04		Lawrence														
34	✓ Wrap Shibboleth w/ UCSD authN	1 day	Wed 4/28/04	Wed 4/28/04	33	Lawrence														
35	✓ Bridge Shib attribute service to UCSD	1 day	Thu 4/29/04	Thu 4/29/04	34	Lawrence														
36	Join InCommon and InQueue	1 wk	Fri 4/30/04	Thu 5/6/04	35	Lawrence														
37	Config Shib for InCommon/InQueue	1 wk	Fri 5/7/04	Thu 5/13/04	36	Lawrence														
38	Integration testing	4 wks	Tue 7/6/04	Mon 8/2/04	37,17	Lawrence														
39	Move origin to production environment	1 wk	Tue 8/3/04	Mon 8/9/04	38	Lawrence														
40	Develop training materials	4 wks	Tue 7/13/04	Mon 8/9/04	38FF+1 wk	Lawrence														
41	Config Blink for Shipp'ed UCFY/YBO	1 wk	Tue 8/10/04	Mon 8/16/04	39,40,13	Lawrence														
42	UCI	80 days	Mon 4/26/04	Mon 8/16/04	12															
43	✓ Install dedicated server to host Shibboleth	1 day	Tue 4/27/04	Tue 4/27/04		Roode,Arseniev														
44	✓ Install Apache, Tomcat Java server, Sun J	1 day	Wed 4/28/04	Wed 4/28/04	43	Roode,Arseniev														
45	✓ Install Shibboleth v1.1	1 day	Thu 4/29/04	Thu 4/29/04	44	Roode,Arseniev														
46	✓ Obtain web server certificate from HEPKI	1 day	Fri 4/30/04	Fri 4/30/04	45	Roode,Arseniev														
47	✓ Join the InQueue federation	1 day	Mon 5/3/04	Mon 5/3/04	46	Roode,Arseniev														
48	✓ Configure Shibboleth Origin	1 wk	Tue 5/4/04	Mon 5/10/04	47	Roode,Arseniev														
49	✓ Set up OpenLDAP database using eduPei	5 wks	Tue 5/11/04	Mon 6/14/04	48	Roode,Arseniev														
50	✓ Test with InQueue	1 wk	Tue 6/15/04	Mon 6/21/04	49	Roode,Arseniev														
51	Integration testing	4 wks	Tue 7/6/04	Mon 8/2/04	50,17	Roode,Arseniev														
52	Move to production environment	1 wk	Tue 8/3/04	Mon 8/9/04	51	Roode,Arseniev														
53	Develop training materials	4 wks	Tue 7/13/04	Mon 8/9/04	51FF+1 wk	Roode,Arseniev														
54	Create Shibbolized links to YCFY/YBO fro	1 wk	Tue 8/10/04	Mon 8/16/04	52,53,13	Roode,Arseniev														
55	Join the InCommon federation when ready	0 days	Mon 4/26/04	Mon 4/26/04		Roode,Arseniev														
56	UCLA	80 days	Mon 4/26/04	Mon 8/16/04	12															
57	✓ Install Test Shibboleth Origin in the Techn	1 day	Tue 4/27/04	Tue 4/27/04		Mahabalagiri														
58	✓ Modify Shibboleth Handle Service to work	1 day	Wed 4/28/04	Wed 4/28/04		Mahabalagiri														
59	Create a prototype directory to provide dai	15 days	Tue 4/27/04	Mon 5/17/04		Ma														
60	Upgrade test Shibboleth Origin to pilot-wo	15 days	Wed 4/28/04	Tue 5/18/04	57	Mahabalagiri														

Project: UC Federated Authentication Date: Tue 6/15/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

FedAuth-2004-06-15

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Calendar															
							11/9	12/28	2/15	4/4	5/23	7/11	8/29	10/17	12/5							
61	Modify the prototype directory to match UC	15 days	Tue 5/18/04	Mon 6/7/04	59	Ma																
62	Upgrade prototype directory to pilot-worthy	15 days	Tue 5/18/04	Mon 6/7/04	59	Ma																
63	Test pilot Shibboleth Origin with YBO and	4 wks	Tue 7/6/04	Mon 8/2/04	60,62,17	Mahabalagiri, Ma																
64	Develop user education materials.	4 wks	Tue 7/13/04	Mon 8/9/04	63FF+1 wk	Mahabalagiri, Ma																
65	Develop support documentation / Train su	4 wks	Tue 7/13/04	Mon 8/9/04	63FF+1 wk	Mahabalagiri, Ma																
66	Rollout the pilot.	1 wk	Tue 8/10/04	Mon 8/16/04	63,64,65,13	Mahabalagiri, Ma, V																
67	Join InCommon.	0 days	Mon 4/26/04	Mon 4/26/04		Wu, Worth																
68	Service Available	0 days	Mon 8/16/04	Mon 8/16/04	32,42,56,24																	
69	Evaluation	60 days	Tue 8/17/04	Mon 11/8/04	68																	
70	Technology Implications	2 mons	Tue 8/17/04	Mon 10/11/04																		
71	Support Implications	2 mons	Tue 8/17/04	Mon 10/11/04																		
72	Organizational Implications	2 mons	Tue 8/17/04	Mon 10/11/04																		
73	Risk Analysis	2 wks	Tue 10/12/04	Mon 10/25/04	70,71,72																	
74	Policy Recommendations	2 wks	Tue 10/26/04	Mon 11/8/04	73																	
75	Follow-On Recommendations	2 wks	Tue 10/26/04	Mon 11/8/04	73																	

Project: UC Federated Authentication Date: Tue 6/15/04	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
